

**Detroit Construction & Demolition Newsletter** 

As of **May 31, 2024** 

### **STABILIZATION**

The Construction & Demolition
Department created the Vacant
Property Unit. This unit will use
Prop N funds to clear out & secure
vacant homes.



## **PROGRESS**

2,022 Completed Trash Out's

3,907 Clear Board Installations

2,262 Completed Stabilizations

1,233 Completed Board-ups
so far in 2024

# OUR PARTNERS THANK YOU!

**1st Choice Hauling AW Preservation Bing Youth Institute Cleaning Up Detroit Detroit Grounds Crew Gayanga GTJ Consulting/MWV Huntman Transport** J. Keith Construction **Emerging Industries Training Institute Motor City Preservation Payne Landscaping Premier Group** P & P Group **Resourceful Vending RT Contracting** Staffing Equipment Evolution

### **CLEAR BOARDS**

Our Securing Team uses Polycarbonate Clear Board, a superior material for boarding, offering strength, durability, and aesthetic appeal beyond traditional options like plywood or metal.





## Demo Dashboard Overview





7,383

HOMES CONTRACTED USING BOND FUNDING

0

HOMES CURRENTLY OUT FOR BID

392

PENDING ABATEMENT

6,349

HOMES DEMOLISHED

642


READY FOR DEMOLITION

6180

**DEMOLITIONS THAT HAVE BEEN GRADED** 



As of 5/31/2024

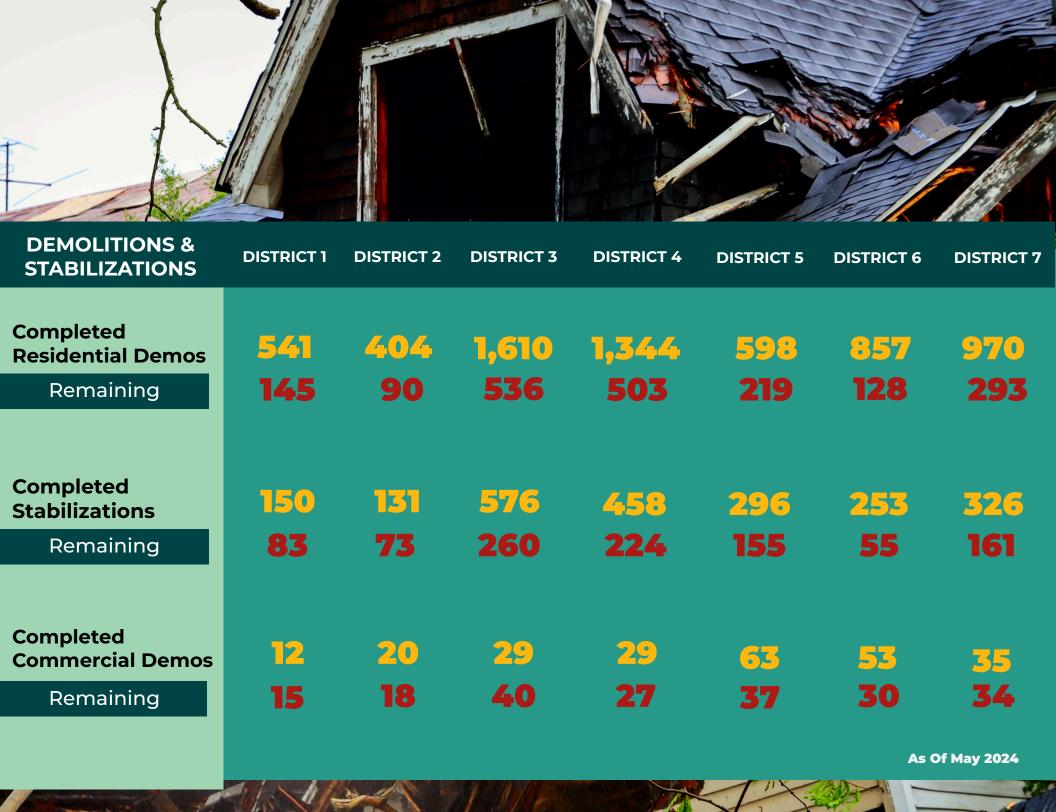



# May Metrics

## **Emergency Demolition Performance**

Demolition Contractor	EMG Count	Within EMG Timeline
DMC Consultants	10	40%
Inner City Contracting, LLC	5	100%
Leadhead Construction	2	100%

## May 2024 Payments

Contractor	Sum of Amount Paid
3D WRECKING LLC	146168.5
ADAMO DEMOLITION COMPANY	1337209.75
AKT PEERLESS ENVIRONMENTAL SERVICES LLC	12800
ATC GROUP SERVICES	19034.5
Beam, Longest and Neff, LLC	113935
Blue Star, Inc.	2500
DLZ	72086
DMC CONSULTANTS INC	641461.19
Environmental Testing & Consulting Inc	8340
GAYANGA CO	1700209.45
GTJ CONSULTING LLC	424685
HOMRICH	296903.26
Inner City Contracting, LLC	1363044
J Keith Construction LLC	123229.5
Juniors JRS Construction	14991
Grand Total	\$7,622,012.68


Account Name	Date Issued	Infraction Type	Contractor Violation: Contractor Violation Name	Notes	Notice of Appeal Date	Outcome of Hearing	Disqualification Start Date	Disqualification End Date	
Able Demolition									
				Wrongful Knock-2008 W. Davison. Discovered by Construction and Demo Planning Specialist while processing an emergency order in 2023. Property					
				knocked on 6/19/2015. It was determined to be wrongfully demo'd by Able.					
Adamo Group, Inc.	10/3/2023	Other	VIO-000734	2000 W. Davison was contracted.					
Adamo Group, inc.				Multiple violations: 1) Missed Planned Knock Down and 2) Fencing					
				inspections not requested as requested in advance. Property-5174 W. Grand					
	9/20/2023	Warning	VIO-000728	River.  Missed Commercial Benchmarks-Bond Groups-203 & 207. Letter rescinded					
	10/11/2023	Warning	VIO-000788	due to missing permits.					
Blue Star	4/5/2024	Warning	VIO-000789	Missed Commercial Benchmarks.					
blue stai				Over 14 Days since OH approved no WG/FG Grade request-7 properties. Did					
	6/22/2023	LOD - Non-Salesforce	VIO-000695	not appeal.		Substantiated			
	6/23/2023	LOD - Non-Salesforce	VIO-000696	Outstanding Winter Grade properties-34. Did not appeal  Outstanding Winter Grade properties-31. 2nd LOD for this type of violation.		Substantiated			
	7/5/2023	LOD - Non-Salesforce	VIO-000700	Did not appeal.		Substantiated			
	7/13/2023	LOD - Non-Salesforce	VIO-000702	Over 14 Days since OH approved no FG Grade request-12 properties.  Substantiated by deputy director on 8/3/2023-46 days (9/18/2023).	7/20/2023	Substantiated	8/3/2023	9/18/2023	
	9/26/2023	Warning	VIO-000731	Missing water pipe material-11 properties.	772072023	Substantiated	0/3/2023	3/10/2023	
Detroit Next	11/7/2023	Warning	VIO-000745	Over 14 Days since OH approved no FG Grade request-4 properties.					
Detroit Next				Outstanding Winter Grade properties-5 properties. Requested an appeal.					
	8/14/2023	LOD	VIO-000716	UnSubstantiated by director.	9/13/2023	UnSubstantiated			
	12/8/2023	Warning	VIO-000753	Warning-Missed Term of Performance for Emergency Property-19608  Coventry.					
DMC Consultants	, 5, 2025		350,33	22.2007					
	7/20/2023	Warning	VIO-000704	Warning-potential wrongful knock-5802 Maryland. Use of wrong photos.		Other			
	7/20/2023	Warning	VIO-000704 VIO-000707	Over 14 Days since OH approved-no FG request-9 properties.		Other			
				Out 14 Days in a Oll second of 50					
	8/1/2023	LOD - Non-Salesforce	VIO-000711	Over 14 Days since OH approved-no FG request-15 properties.Requested a Final appeal. Next violation will result in automatic LOD.	9/7/2023	UnSubstantiated			
	8/23/2023	Warning	VIO-000721	Missing hydrant addresses for 13 properties. Corrected the same day.  Properties (19) Over 14 Days since Open Hole Approved-no Final Grade					
	10/25/2023	Warning	VIO-000743	requested.					
	11/7/2023	Warning	VIO-000746	Properties (22) Over 14 Days since Open Hole Approved-no Final Grade requested.					
	11///2023	warning	VIO-000746	Over 14 Days since OH approved-no FG request-18 properties. Due to a					
		LOD - Non-Salesforce	VIO-000759	history of this type of violation it resulted in an automatic LOD.		Substantiated			
	2/12/2024	Warning	VIO-000769	Warning-missing Water Pipe Material information-12 properties.  Missed an Demo Performance Benchmark-2 (50%) for Bond Groups		Other			
	4/29/2024	Warning	VIO-000792	Q1&2.See attached Salesforce report.					
	5/13/2024	Warning	VIO-000796	Missed EMG timeline on a property located at 17144 Harlow.  A section of asphalt near 5968 Seminole, between Lambert and Medbury,					
				was damaged. See attached pictures. DMC has acknowledged responsibility					
Gayanga Co. LLC	6/17/2024	LOD - Non-Salesforce	VIO-000806	for this damage. Appealed.	6/17/2024				
Gayanga Go. LLG				Violations:19129 Teppert-1. Failure to adequately wet ACWM. 2. Failure to					
	- /. /			dispose of ACWM as soon as practical.Appealed 8.8.23. Final Decision is on	- /- /				
	8/1/2023	EGLE	VIO-000708	Hold.  Failure to wait for verification on the PASV Smartsheet before starting	8/8/2023				
	10/23/2023	Warning	VIO-000741	abatement work-7123 Chatfield.		Other			
	2/13/2024	Warning	VIO-000775	Missed Abatement Performance Milestones-1 (25%) for Bond Groups Q10 and Q11.		Other			
				Missed Demolition Performance Milestones-1 (25%) for Bond Groups Q10,					
	2/21/2024	Warning	VIO-000776	Q11 & Q12.		Other			
				Health and Safety Violation: Failure to Remove or Report asbestos containing waste material-floor tile to Demolition Department. Deputy					
	2/29/2024	HSV-3D	VIO-000779	Director unsubstantiated violation.	2/29/2024	UnSubstantiated			
	3/27/2024	Warning	VIO-000786	Over 7 days since knock-no OH request.		Other			
				Missed Abatement Performance Milestones-1 (50%) for Bond Groups Q10					
Hamrich	5/3/2024	Warning	VIO-000791	and Q11. They had abatement issues in Jan and Feb 2024.		Other			
- Frontien				1. Failure to Cooperate, Coordinate and Communicate with Field Operation					
				team.					
	8/17/2023	LOD	VIO-000718	<ol> <li>Failure to perform demo services within the Days and Hours of Operation.</li> <li>Appealed.</li> </ol>	8/24/2023	Substantiated			
				Properties over 14 Days since Open Hole approved-no FG request-21					
	9/13/2023	LOD	VIO-000725	properties.Hearing with Tim on 10/5/23-Unsubstantiated. Only 1 property remaining on 10/5/23.	9/20/2023	UnSubstantiated			
	9/22/2023	Warning	VIO-000729	Commercial properties that missed 1 or more benchmarks.	., .,				
	6/12/2024	Warning	VIO-000804	Warning: damage of fencing at 7575 Palmetto due to the collapse of the property's exterior rear wall.					
Inner City Contracting, LLC		AA GI IIII IS							
	6/29/2023	Warning	VIO-000735	Commercial properties that missed 1 or more benchmarks.					
				Violations: 10920 Shoemaker-1. Failure to adequately wet ACWM. 2. Failure to dispose of ACWM as soon as practical. Appealed. Final Decision on Hold					
	7/31/2023	EGLE	VIO-000712	from appeals board.	8/7/2023				
	9/25/2023	Warning	VIO-000730	Missing fencing on sides C&D at 4405 Cadillac.					
	10/20/2023	Warning	VIO-000740	Failed to timely enter the Start and Finish dates on the PASV Smartsheet.					
	12/8/2023	Warning	VIO-000755	Missed an emergency timeline for a property at 11850 Van Dyke.					
		Warning	VIO-000755 VIO-000757	Missed an emergency timeline for a property at 11850 Van Dyke.  Missed entering the knock-down date for 11850 Van Dyke into Salesforce within one business after knock.					

	1/10/2024							
		Warning	VIO-000761	Over 14 Days since Open Hole-No FG request-20 properties				
	1/29/2024	Warning	VIO-000763	Missing abatement details for 55 properties.				
	2/0/2024	Other	1//0 000781	Conference Call Record: Contractor failed to Failure to submit Emergency				
	2/9/2024 2/12/2024	Other Warning	VIO-000781 VIO-000768	Demolition Fence Plans in a timely fashion.  Missed entering the Planned knock-down date for 4 properties.				
	2/15/2024	Warning	VIO-000768 VIO-000799	Properties over 30 days				
	2/15/2024	Warning	VIO-000800	Properties over 30 days				
	2/21/2024	Warning	VIO-000777	Missed Demolition Benchmark-1 (25%) Bond Group Q20.				
				Conference Call Record: Contractor failed to verify location of scheduled				
				demolition. Without intervention from DCDD Field Liaison, the wrong				
				property would have been knocked. See attached conference record from				
	2/29/2024	Other	VIO-000780	Linda Montgomery.				
				Conference Call Record: Subject: Miscommunication between ICC and demo				
				team. They changed their fencing plan without informing demo team. Not a				
	3/22/2024	Other	VIO-000784	recurring event.				
				Missed an Abatement Performance Benchmark-2 (50%) for Bond Group Q3.				
	3/25/2024	Warning	VIO-000785	Abatements rolling complete-43. Abatement rolling pct-44%.				
				Violations: 7757 Rosemont-1. Failure to remove all RACM. 2. Failure to				
	4/40/2024	5015	140 000700	adequately wet RACM. Violation substantiated on 5/2/24 by Deputy.  Requested Final Board hearing with Director.	F (0 (2024			
J Keith Construction	4/18/2024	EGLE	VIO-000790	Requested Final Board hearing with Director.	5/9/2024			
J Keith Construction	6/26/2023	Warning	VIO-000697	Missing Water Pipe information-9 properties.				
	0/20/2023	warriing	VIO-000057	Damage to adjacent property's driveway. Assigned demo property was				
	7/5/2023	Warning	VIO-000701	14779 Petoskey. Damaged property was 14779 Petoskey.				
	8/2/2023	Warning	VIO-000701	Over 14 Days since Open Hole approved no FG request-5 properties.				
	0/2/2023	www.iiiiig	V10*000710	Company Asbestos Abatement Contractor License has expired.Released				
	8/3/2023	Stop Work	VIO-000713	from SWO on 8/9/2023.				
	5,5,2025	2.25 1101%	1.0 000/13					
				Missed Demo 4 Benchmark dated 8/18/23. Demo was 26% of 100%. Only 21				
				out of 81 properties knocked. Released from Stop Work (4/7/23 to 4/12/23				
	8/18/2023	LOD - Non-Salesforce	VIO-000720	& 8/3/23 to 8/9/23)-Final Appealed.Did not attend final appeal.	9/15/2023	Substantiated		
				Failure to update Salesforce with the Knock Down Date in a timely manner.				
				Property was knocked on 10/4/23. Entered into SF on 10/16-12381				
	10/16/2023	Warning	VIO-000737	Wisconsin.				
				Missed Final Grade Benchmark-4 dated 10/13/23. FG was 28% of 100%.				
	10/17/2023	LOD - Non-Salesforce	VIO-000739	Only 23 out of 81 properties were FG.	10/23/2023	Substantiated		
				Missed Demolition Benchmark-4 dated 12/6/2023. Demo rolling completed-				
				46% of 100%. Only 37 out of 81 properties completed. Demo benchmark				
				ended on 12/8/2023. Substantiated by Deputy Dir. on 1/4/24. No Final				
	12/6/2023	LOD - Non-Salesforce	VIO-000752	appeal requested.	12/11/2023	Substantiated		
	4 /0 /2024	14/	VIO-000760	Missed Planned Knock Down date. Property located at 15774 Mendota.				
	1/8/2024	Warning	VIO-000760					
				Missed Demolition Benchmark-4 dated 1/29/2024. Demo rolling completed- 51% of 100%. Only 41 out of 81 properties completed. Demo benchmark				
	1/29/2024	LOD - Non-Salesforce	VIO-000762	ended on 12/8/2023.Did not final appeal.		Substantiated		
	2/12/2024	Warning	VIO-000767	Failure to update Planned Knock Down dates for 3 properties.		Substantiated		
	2,12,2024	· · · · · · · · · · · · · · · · · · ·	110 000707	Tallace to apade Trainies Riock Sown saces for 5 properties.				
				Missed Demolition Benchmark-4 (100%). Demo rolling completed-56% of				
				Missed Demolition Benchmark-4 (100%). Demo rolling completed-56% of 100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on				
	2/28/2024	LOD - Non-Salesforce	VIO-000778	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on	3/5/2024	Substantiated	3/28/2024	9/27/2024
		LOD - Non-Salesforce Warning	VIO-000778 VIO-000787	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.	3/5/2024	Substantiated	3/28/2024	9/27/2024
	2/28/2024 4/9/2024			100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on	3/5/2024	Substantiated	3/28/2024	9/27/2024
				100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned Knock Down dates for a property.	3/5/2024	Substantiated	3/28/2024	9/27/2024
				100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demo'd 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.	3/5/2024	Substantiated  Substantiated	3/28/2024 5/8/2024	9/27/2024 5/8/2025
	4/9/2024	Warning  LOD - Non-Salesforce	VIO-000787 VIO-000794	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property.  Missed Demolition Benchmark-4 (100%). Demo rolling completed-79% of 100%. Demo'd 63 out of 81 properties completed. Sixth LOD Issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the	3/5/2024			
	4/9/2024	Warning	VIO-000787	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demo'd 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.	3/5/2024			
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024	Warning  LOD - Non-Salesforce  Stop Work	VIO-000787 VIO-000794 VIO-000803	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demo'd 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.	3/5/2024			
Leadhead Construction	4/9/2024	Warning  LOD - Non-Salesforce	VIO-000787 VIO-000794	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark-4 (100%). Demo rolling completed-79% of 100%. Demo'd 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.	3/5/2024			
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning	VIO-000787 VIO-000794 VIO-000803 VIO-000706	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement	3/5/2024			
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 6 63 out of 81 properties completed. Sixth LD0 issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demol 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont		Substantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning	VIO-000787 VIO-000794 VIO-000803 VIO-000706	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol' of 3 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F. 2995 Clairmont Failure to maintain fending at 8896 & 8925 Kimberly. Appealed.	3/5/2024 9/1/2023			
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned Knock Down dates for a property.  Missed Demolition Benchmark 4 (100%), Demo rolling completed-79% of 100%. Demo'd 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont  Failure to maintain fencing at 8896 & 8925 Kimberly, Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark		Substantiated  UnSubstantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD Issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom Fr. 2995 Clairmont Failure to maintain fencing at 8896 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal.		Substantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor di 63 out of 81 properties completed 5:kth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestona 3 (75%). Attained only 44.44%.		Substantiated  UnSubstantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned Knock Down dates for a property.  Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demo'd 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demol 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fending at 8896 & 8925 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark date was 9/2/2/2023. Did not appeal.  Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not		Substantiated  UnSubstantiated  Substantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demoltion Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD Issued on 4/30/24. Did not appeal. 365 days sup. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F-2995 Clairmont Failure to maintain fending at 8896 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Joh not appeal. Missed a Final Grade Performance Milestone 3 (75%), Attained only 44.44%, Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal-		Substantiated  UnSubstantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 8895 & 8295 Kimberly, Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestona e 175%). Attained only 44.44%. Benchmark date was 11/10/203. Substantiated by deputy-11/30. Did not appeal-due on 12/8/23. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final		Substantiated  UnSubstantiated  Substantiated		
Leadhead Construction	4/30/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned Knock Down dates for a property.  Missed Demoltion Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD Issued on 4/30/24. Did not appeal. 365 days sup. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fending at 8896 & 8925 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark date was 9/22/2023. Did not appeal.  Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 14/2024, none of the previous properties were on the	9/1/2023	Substantiated  UnSubstantiated  Substantiated  Substantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned knock Down dates for a property.  Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor di 50 uto f 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal.  Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal-due on 12/8/23.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.		Substantiated  UnSubstantiated  Substantiated		
Leadhead Construction	4/30/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned knock Down dates for a property.  Missed Demolition Benchmark 4 (100%), Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth 100 issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 8896 & 8925 Kimberly, Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal.  Missed a Final Grade Performance Milestona 3 (75%). Attained only 44.44%, Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal-due on 12/8/23.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties.	9/1/2023	Substantiated  UnSubstantiated  Substantiated  Substantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned knock Down dates for a property.  Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor di 50 uto f 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal.  Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal-due on 12/8/23.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.	9/1/2023	Substantiated  UnSubstantiated  Substantiated  Substantiated		
Leadhead Construction	4/30/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demoltion Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days sup. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F-2995 Clairmont Failure to maintain fending at 8896 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties. Request for affidavit due to altered Asbestos Waste Manifest submitted to	9/1/2023	Substantiated  UnSubstantiated  Substantiated  Substantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000758	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned knock Down dates for a property.  Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor dis 30 ut of 81 properties completed 5:kth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 8896. 8295 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark date was 9/12/2023. Did not appeal.  Missed a Final Grade Performance Milestona 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal appeal-due on 12/8/23.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties.  Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000758	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned knock Down dates for a property.  Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor dis 30 ut of 81 properties completed 5:kth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 8896. 8295 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark date was 9/12/2023. Did not appeal.  Missed a Final Grade Performance Milestona 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal appeal-due on 12/8/23.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties.  Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000758	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor di 50 at or 61 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal-due on 12/8/23. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties. Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
Leadhead Construction	4/30/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning  Warning  UOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000758  VIO-000765  VIO-000802	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor dis 30 ut of 81 properties completed Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal-due on 12/8/23. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce 12 properties. Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics. Improper Disposal of Debris in Alleyway-6886 Parkwood. Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated LOD. It was discovered that an emergency demo notification with an incorrect	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024 5/7/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  UOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning  Warning  Warning  Warning	VIO-000787  VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000755  VIO-000755  VIO-000802  VIO-000797	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property.  Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD Issued on 4/30/24. Did not appeal. 365 days sup. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F-2995 Calirmont Failure to maintain fencing at 8896 & 8925 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark date was 9/22/2023. Did not appeal.  Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties.  Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics.  Improper Disposal of Debris in Alleyway-6886 Parkwood.  Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated LOD. It was discovered that an emergency demonistrication with an incorrect address was submitted to ECIL to demolish the property at 14607	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024 5/7/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning  Warning  UOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000758  VIO-000765  VIO-000802	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor dis 30 ut of 81 properties completed Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal-due on 12/8/23. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce 12 properties. Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics. Improper Disposal of Debris in Alleyway-6886 Parkwood. Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated LOD. It was discovered that an emergency demo notification with an incorrect	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
Leadhead Construction	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024 5/7/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  UOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning  Warning  Warning  Warning	VIO-000787  VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000755  VIO-000755  VIO-000802  VIO-000797	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor dis 30 ut of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 8896. 88295 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark date was 9/12/2023. Did not appeal. Missed a Final Grade Performance Milestona 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal the substantial of the deformance of the previous properties were on the Salesforce report. Missing Water Hydrant addresses in Salesforce-12 properties. Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics. Improper Disposal of Debris in Alleyway-6886 Parkwood.  Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated LOD. It was discovered that an emergency demo notification with an incorrect address was submitted to EGLE to demolish the property at 14607 Northlawn.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/2024 5/7/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning  LOD - Non-Salesforce  Warning  LOD - Non-Salesforce	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000758  VIO-000765  VIO-000802  VIO-000797	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property. Missed Demoltion Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days sup. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F-2995 Clairmont Failure to maintain fending at 8896 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal. Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal due on 12/8/23. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report. Missing Water Hydrant addresses in Salesforce-12 properties. Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics. Improper Disposal of Debris in Alleyway-6886 Parkwood. Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated LOD. It was discovered that an emergency demo notification with an incorrect address was submitted to EGLE to demolish the property at 14607 Northlawn.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024 5/7/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  UOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning  Warning  Warning  Warning	VIO-000787  VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000755  VIO-000755  VIO-000802  VIO-000797	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor dis 30 ut of 81 properties completed. Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal-due on 12/8/23. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties. Request for affidavit due to altered Absetos Waste Manifest submitted to Livegistics. Improper Disposal of Debris in Alleyway-6886 Parkwood.  Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated LOD. It was discovered that an emergency demo notification with an incorrect address was submitted to EGLE to demolish the property at 14607 Northlawn.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024 5/7/2024 6/12/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  UOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  UOD - Non-Salesforce  Warning  Warning  UOD - Non-Salesforce  Warning  UOD - Non-Salesforce  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000747  VIO-000747  VIO-000756  VIO-000758  VIO-000755  VIO-000802  VIO-000805  VIO-000805	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned Knock Down dates for a property.  Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demol 63 out of 81 properties completed. Sixth LOD Issued on 4/30/24. Did not appeal. 365 days sup. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Calirmont Failure to maintain fending at 8896 & 8925 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment. Benchmark date was 9/22/2023. Did not appeal.  Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 14/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties.  Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics.  Improper Disposal of Debris in Alleyway-6886 Parkwood.  Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated LOD. It was discovered that an emergency demo notification with an incorrect address was submitted to EGLE to demolish the property at 14607 Northlawn.  Over 14 Days since Open Hole approval-No Final Grade request-9 properties.  Over 14 Days since Open Hole approval-No Final Grade request-9	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
	4/9/2024  4/30/2024  6/6/2024  7/25/2023  8/15/2023  8/15/2023  11/17/2023  12/11/2023  12/11/2023  2/2/2024  5/7/2024  5/29/2024  6/12/2024  7/25/2023  8/9/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning  Warning  UOD - Non-Salesforce  Warning  Warning  UOD - Non-Salesforce  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000758  VIO-000765  VIO-000802  VIO-000797  VIO-000805	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor di 63 out of 81 properties completed. Sith LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F. 2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal. appeal-due on 12/8/23. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties. Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics.  Improper Disposal of Debris in Alleyway-6886 Parkwood.  Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated U.D. It was discovered that an emergency demo notification with an incorrect address was submitted to EGLE to demolish the property at 14607 Northlawn.  Over 14 Days since Open Hole approval-No Final Grade request-9 properties.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
	4/9/2024 4/30/2024 6/6/2024 7/25/2023 8/15/2023 8/30/2023 9/29/2023 11/17/2023 12/11/2023 12/13/2023 2/2/2024 5/7/2024 6/12/2024	Warning  LOD - Non-Salesforce  Stop Work  Warning  UOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  UOD - Non-Salesforce  Warning  Warning  UOD - Non-Salesforce  Warning  UOD - Non-Salesforce  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000722  VIO-000747  VIO-000747  VIO-000756  VIO-000758  VIO-000755  VIO-000802  VIO-000805  VIO-000805	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months.  Failure to update Planned knock Down dates for a property.  Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor dis 30 ut of 81 properties completed Sixth LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25.  A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023.  Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed.  Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal.  Missed a Final Grade Performance Milestona 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal due on 12/8/23.  Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydranta addresses in Salesforce-12 properties.  Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics.  Improper Disposal of Debris in Alleyway-6886 Parkwood.  Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated LOD.  It was discovered that an emergency demo notification with an incorrect address was submitted to EGLE to demolish the property at 14607 Northlawn.  Over 14 Days since Open Hole approval-No Final Grade request-9 properties.  Over 14 Days since Open Hole approval-No Final Grade request-9 properties.  Warning-Missing Water Pipe material-9 properties.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		
	4/9/2024  4/30/2024  6/6/2024  7/25/2023  8/15/2023  8/15/2023  11/17/2023  12/11/2023  12/11/2023  2/2/2024  5/7/2024  5/29/2024  6/12/2024  7/25/2023  8/9/2023	Warning  LOD - Non-Salesforce  Stop Work  Warning  Warning  LOD - Non-Salesforce  LOD - Non-Salesforce  LOD - Non-Salesforce  Warning  Warning  Warning  UOD - Non-Salesforce  Warning  Warning  UOD - Non-Salesforce  Warning	VIO-000787  VIO-000794  VIO-000803  VIO-000706  VIO-000719  VIO-000733  VIO-000747  VIO-000756  VIO-000756  VIO-000758  VIO-000765  VIO-000802  VIO-000797  VIO-000805	100%. Only 45 out of 81 properties completed. Deputy Dir. substantiated on 3/15/24. On 3/28/24, suspended by Director for 6 months. Failure to update Planned knock Down dates for a property. Missed Demolition Benchmark 4 (100%). Demo rolling completed-79% of 100%. Demor di 63 out of 81 properties completed. Sith LOD issued on 4/30/24. Did not appeal. 365 days susp. Ends 5/8/25. A number of sites that have exceeded their time frames as stipulated in the Scope of Services.  Missed Demo 2 (50%) benchmark. Dated 7/14/2023. Failure to remove poly at demo site. City Abatement was the abatement contractor. Email sent by Tom F. 2995 Clairmont Failure to maintain fencing at 886 & 8925 Kimberly. Appealed. Missed Demo 3 (75%) benchmark with only a 42% attainment.Benchmark date was 9/22/2023. Did not appeal. Missed a Final Grade Performance Milestone 3 (75%). Attained only 44.44%. Benchmark date was 11/10/2023. Substantiated by deputy-11/30. Did not appeal. appeal-due on 12/8/23. Sixteen (16) properties that are over 14 Days Since Open Hole-no Final Grade Request. As of 1/4/2024, none of the previous properties were on the Salesforce report.  Missing Water Hydrant addresses in Salesforce-12 properties. Request for affidavit due to altered Asbestos Waste Manifest submitted to Livegistics.  Improper Disposal of Debris in Alleyway-6886 Parkwood.  Work plan for adjacent emergency properties is unacceptable. Reason are attached. If this issue occurs in the future it will incur a substantiated U.D. It was discovered that an emergency demo notification with an incorrect address was submitted to EGLE to demolish the property at 14607 Northlawn.  Over 14 Days since Open Hole approval-No Final Grade request-9 properties.	9/1/2023	Substantiated  UnSubstantiated Substantiated Substantiated UnSubstantiated		

				Over 14 Days since Open Hole approval-No Final Grade request-1 property-				
	10/25/2022	LOD - Non-Salesforce	VIO-000742	17195 Arlington. Appealed. Substantiated by deputy-11/30/2023.Did not final appeal by 12/8/2023.	11/1/2023	Substantiated		
RDC Construction Services	10/25/2023	LOD - Non-Salestorce	VIO-000742	Imai appeal by 12/8/2023.	11/1/2023	Substantiated		
RDC Construction Services				Violations: 2249 Fairview-1. Failure to adequately wet ACWM. 2. Failure to				
				dispose of ACWM as soon as practical. Substantiated by Deputy. Did not				
	8/1/2023	EGLE	VIO-000709	request final appeal.	8/8/2023	Substantiated	9/16/2023	11/15/2023
	0/1/2023	LULL	VIO-000703	request intal appeal.	0/0/2023	Jubstantiateu	3/10/2023	11/13/2023
	8/30/2023	Warning	VIO-000723	Failed to update the hydrant addresses in a timely manner-8 properties.				
				Over 14 Days since OH approved-no FG request-5 properties. Did not				
	9/14/2023	LOD - Non-Salesforce	VIO-000727	appeal.		Substantiated		
Salenbien Trucking & Excavating Inc.								
	7/5/2023	Warning	VIO-000699	Uncovered Demo debris over 24 hrs-12538 Goulburn.				
				Violations: 12538 Goulburn-1. Failure to adequately wet ACWM. 2. Failure				
				to dispose of ACWM as soon as practical. Demo issue opened 6/14/23 and				
	7/31/2023	EGLE	VIO-000714	closed on 7/14/23.	8/2/2023	UnSubstantiated		
SC Environmental Services, LLC								
				Wrongful Knock-17191 Justine-Contractor error-failure to validate address.				
				Both properties are under contract with SC Environmental. Employee				
	- / /			suspended w/o pay. Other employees issued Warning letters. Policy				
	9/28/2023	Other	VIO-000732	updated. Did not appeal.		Substantiated		
				Wrongful Knock-19636 Albany.19652 Albany was the contracted property.				
	44 /24 /2022	Other	VIO-000748	Both properties are DLBA owned. Will not appeal.60 Day Suspension starts			44 (20 (2022	4 /20 /2024
	11/21/2023	Otner	VIO-000748	11/30/2023 and ends 1/29/24		Substantiated	11/30/2023	1/29/2024
				Over 14 Days since Open Hole approval-No Final Grade request-17				
	4/29/2024	Warning	VIO-000793	properties. Company is currently working on a restructure of their team.				
	4,25,2024	vvarillig	V10*000755	properties. Company is currently working on a restructure of their team.				
				Wrongful Knock-654 E Savannah. 645 E Savannah was the contracted				
	5/31/2024	Other	VIO-000798	property. The is the third violation within a 365 day period.				
	-, -1, -01	2.3161		property,		-		+

# Detroit Block X Block

Powered by the Construction & Demolition Department

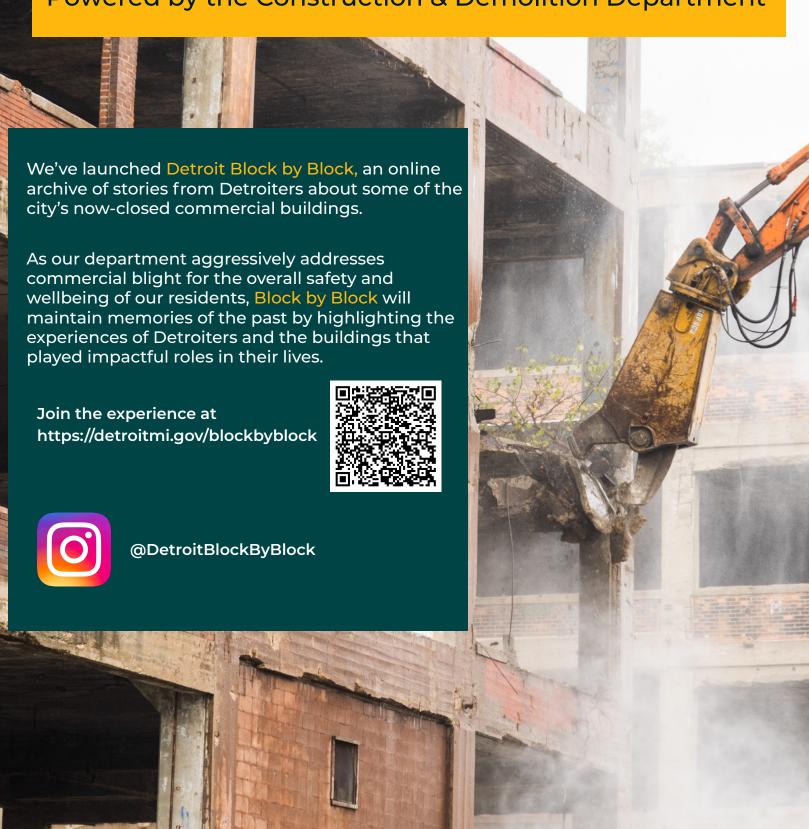



"If you are not going to sell it to anybody that can afford to buy it, and you're not going to fix it up for children to be able to come back, then tear it on down," said Miss Betts, community member and

**CLICK HERE** or scan the QR code below to watch the full interview with Miss. Betts and other community members about the demolition of Lynch Elementary.





### **CONTACT INFORMATION TO KNOW**



### **Detroit Construction and Demolition Department** 313-224-4737

demo-info@detroitmi.gov



#### Report abandoned and/or Dangerous Building 313-224-3215 BSEDDemo@detroitmi.gov



#### **Department of Neighborhoods**

Locate your District Manager at: www.detroitmi.gov/neighborhoods



## EMPLOYEE SPOTLIGHT



"I Am Detroit" highlights the Detroit Construction & Demolition Department team members and their unwavering commitment to serving Detroit's residents.





## **Detroit Demo Social Analytics**







May 1 - May 31

20,370

7,865

1,298

371

89.4%





# Glossary of Terms, Abbreviations, and Acronyms

**3D -- Detroit Demolition Department** 

**COD -- City of Detroit** 

CRIO -- Civil Rights, Inclusion & Opportunity Department

**DESC -- Detroit Employment Solutions Corporation** 

**DLBA** -- Detroit Land Bank Authority

**DON -- Department of Neighborhoods** 

**EMG -- Emergency Demolition** 

**HRD -- Housing and Revitalization Department** 

**HSV** -- Health and Safety Violation

**LOD** -- Letter of Discipline

NIB -- Neighborhood Improvement Bond

NIP -- Neighborhood Improvement Plan

**OCFO** -- Office of the Chief Financial Officer

**OCP -- Office of Contracting and Procurement** 

**ODFS -- Office of Departmental Financial Services** 

**ODM** -- Ordered Demolition



