

CONSTRUCTION UPDATE

January 2024

The Detroit Water and Sewerage Department (DWSD) continues to make construction progress on improvements in your neighborhood. DWSD thanks the community for your patience and support as we work hard to improve your neighborhood. DWSD has the following update on our project in the Far West Detroit neighborhood.

Current Work

Sawyer Street Construction:

Our contractor, Major Contracting, completed installation of a new combined sewer main on Sawyer Street between Parkland and West Parkway.

The contractor began installation of large diameter storm sewer along Sawyer. Construction is currently between Parkland and Rockdale and will continue west toward West Parkway. Sawyer will remain closed to through traffic for the duration of storm sewer installation.

DWSD has been coordinating with the Ann Arbor Trail Magnet School to help ensure that parents, students, and teachers have easy access to the building and parking lot. While construction occurs along Sawyer in front of the school, pick up and drop off access will be maintained from Tireman to the north.

South Basin Earthwork:

The contractor continues to remove the excess excavated soils from the stockpile located east of Outer Drive in Rouge Park, as weather allows. This area will be final graded for restoration in the spring. This work will also involve restoring the bike path impacted by the sewer construction.

Parkland Street Water Main:

Water main replacement work on Parkland Street between West Warren and Tireman will occur this year. This portion of water main was not originally scheduled for replacement. However, based on the number of breaks and the impacts to residents, DWSD has added this section of water main to its replacement schedule under a separate contract.

Belton and West Parkway Sewer:

In late 2023, the contractor began installing storm sewer along Belton between Parkland and West Parkway. Work was suspended in November due to cold weather and a DTE gas main conflict. DWSD anticipates the gas main will be relocated in early spring which will allow work to resume.

Prior to starting these items of work, affected residents will receive written information distributed to adjacent homes. This will provide more details on the duration and impacts of the work.



Map showing current and upcoming work on West Parkway, Belton, Sawyer, and Parkland.




Combined sewer pipe and manholes being installed along Sawyer Street.

Completed Work

The project began in Spring 2022 and is expected to be completed in Fall 2026. Key milestones are noted below.

- The planned water main installations throughout the neighborhood are complete (note that additional work on Parkland will occur in 2024).
- Storm sewer along Majestic, Parkland, and Belton (to Beaverland) is complete.
- The north and south stormwater basins have been graded and restored. Note that areas surrounding the south basin are still under construction awaiting seeding and tree restoration.

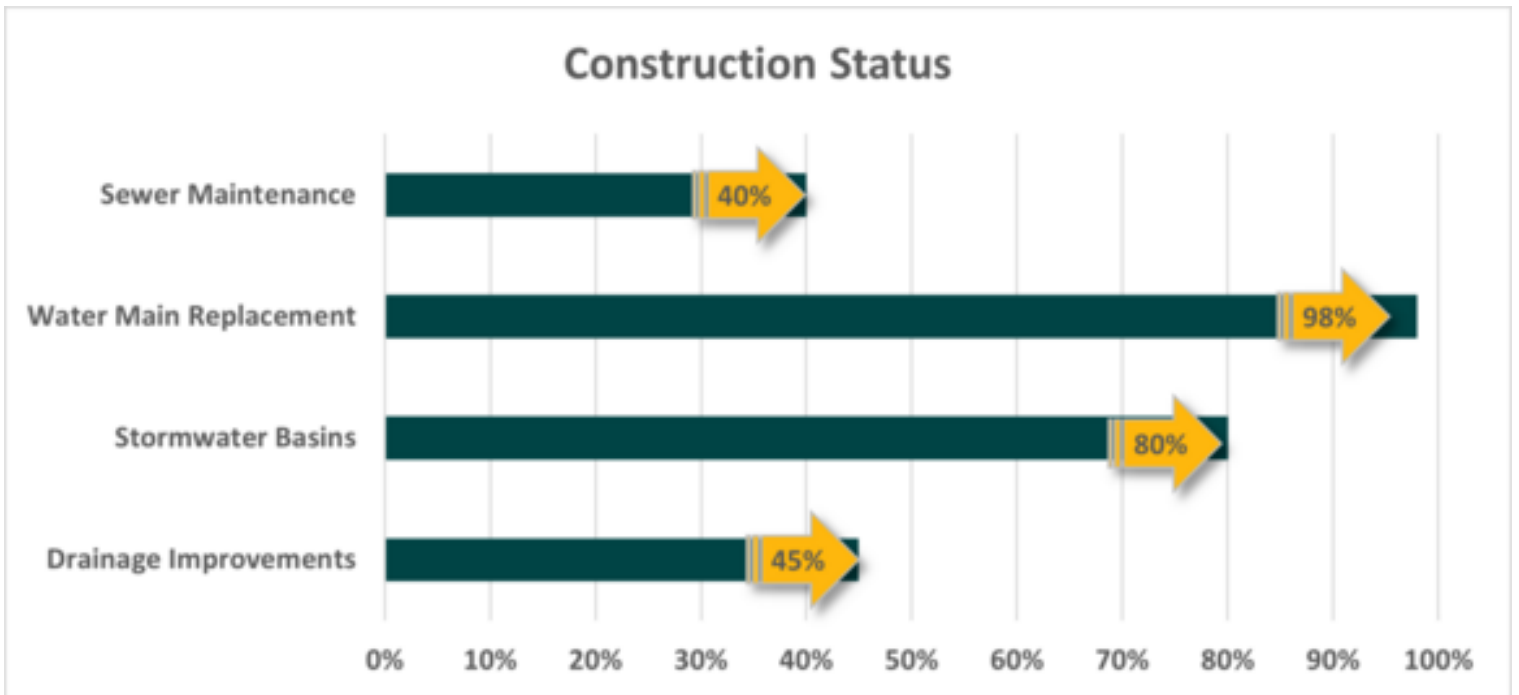

Stay Engaged

There are several ways that you can stay up to date on the Far West Detroit Stormwater Improvement Project.

- **Updates via Email** -Thanks for joining our e-newsletter list. Your neighbors can join our distribution list by sending their name and address to dwsd-publicaffairs@detroitmi.gov. DWSD sends monthly newsletters to this list serv with key project updates. Project updates are also posted on Nextdoor and the [project webpage](#).
- **Phone** - Report any concerns to the Public Affairs Construction Line: 313-880-2812
- **Attend our Project Progress Meetings** - DWSD hosts quarterly neighborhood-wide update meetings. Meeting notices are sent through the email list, Nextdoor and door hangers are distributed to the entire neighborhood.











Thank You!

We know construction projects can be messy, dirty and noisy. The work can also be inconvenient for our residents as you move to and from your homes. **DWSD understands this and appreciates your patience throughout this process as we work to upgrade the infrastructure in your neighborhood.**

DWSD is available to answer your questions or concerns regarding construction in Far West Detroit. If you have a question, please call us at 313-880-2812 or [email us at dwsd-publicaffairs@detroitmi.gov](mailto:dwsd-publicaffairs@detroitmi.gov).

WHAT YOU SHOULD EXPECT

During construction it is DWSD's intention to minimize inconveniences to residents and businesses. However, you should expect the following:

WATER SYSTEM	SEWER SYSTEM
 <p>Brief interruptions of water supply when a new service line is being connected to the system. Every attempt will be made to inform impacted residents and businesses prior to disruption and service is generally restored the same day. Please contact DWSD Customer Care if you do not have water service for more than six hours or overnight.</p>	 <p>You will be notified when your sewer connection will be temporarily plugged. During this time, your sewer system should not be used. Don't use toilets(s), sinks, bathtub/shower, basement drains, dishwasher and clothes washer. This is to prevent backups into your home. You will be notified when your sewer line is safe to use. During this time you will have access to running water.</p>
 <p>Water main work may require some hydrants to be out of service intermittently. These hydrants will be tagged as out of service and DWSD will coordinate with the Detroit Fire Department with up-to-date information.</p>	 <p>Contractors working on sewer pipelines will need to access manholes in backyards and alleys. All manholes need to be accessible – free of vegetation, fencing or other objects. Lawns, cement, fences and other property in the sewer right-of-way may be disturbed. Contractors will return to restore property. Temporary restorations may occur before permanent work is completed during April - October when weather permits.</p>
 <p>Contractors will have large trucks and heavy equipment. For the safety of everyone in the neighborhood, please keep a safe distance from all machinery.</p>	 <p>The community may experience an odor during sewer construction activities.</p>
 <p>Construction will bring some noise, dirt and debris to the neighborhood.</p>	
 <p>There may be traffic impediments, but residents and businesses will have access. You should also expect street closures and restrictions to street parking during construction. Please try to avoid parking on impacted streets.</p>	
 <p>Lawns, sidewalks and driveways may be disturbed. Contractors will return to restore property. Temporary restorations may occur before permanent work is completed during April – October when weather permits.</p>	
 <p>To perform work, contractors may need to trim or cut trees and brush to access streets and alleys.</p>	
