

CONSTRUCTION UPDATE

October 2024

Please see Detroit Water and Sewerage Department (DWSD) construction updates and maps below.

What's Happening in the Neighborhood?

Major Contracting will continue road and lawn restoration before cold weather arrives.

Street Restoration

Major Contracting crews are restoring pavements, driveways and sidewalks on several streets. This work will occur through the next few weeks and will be followed by lawn and sprinkler system repairs. This work is happening on:

- **W Parkway between Parkland and Tireman**
- **Lamphere between Parkland and Tireman**
- **Dacosta between Parkland and Sawyer**

Lawn and Sprinkler Repair

On streets where roadwork is complete, the contractor is performing lawn restoration and sprinkler repair. This work is happening on:

- **Beaverland, Bramell, Tireman, and Chatham**
- **Parkland between Tireman and W Warren** (Work related to the water main replacement project being completed by DWSD's contractor LGC.)

Spring 2025 Work

Storm sewer installation on Dolphin and Tireman will begin in early spring of 2025 once temperatures start to warm.

- **Dolphin between Sawyer and Tireman**
- **Rockdale between Parkland and Sawyer**


What's Happening in Rouge Park?


Contractors continue to work on final grading, topsoil placement and seeding around the south basin in Rouge Park. Planting of the remaining plants and trees will occur in the fall, along with continued maintenance of the prairie grass and flowers.

Additional maintenance and supplemental planting work will also occur in the spring of 2025. Following the completion of this, the bike path along the east shoulder of Outer Drive will be restored to ensure that construction activity does not damage newly placed pavements.

CONSTRUCTION STATUS UPDATE Drainage Work (As of 9/23/2024)

-  **Complete**
(Drainage/sewers installed, pavement placed and grass planted)
-  **Substantially Complete**
(Drainage/sewers installed, pavement placed, awaiting restoration)
-  **In Progress**
(Sewers installed or being placed, awaiting pavement and restoration)
-  **Upcoming**
(Work yet to be completed under this contract)

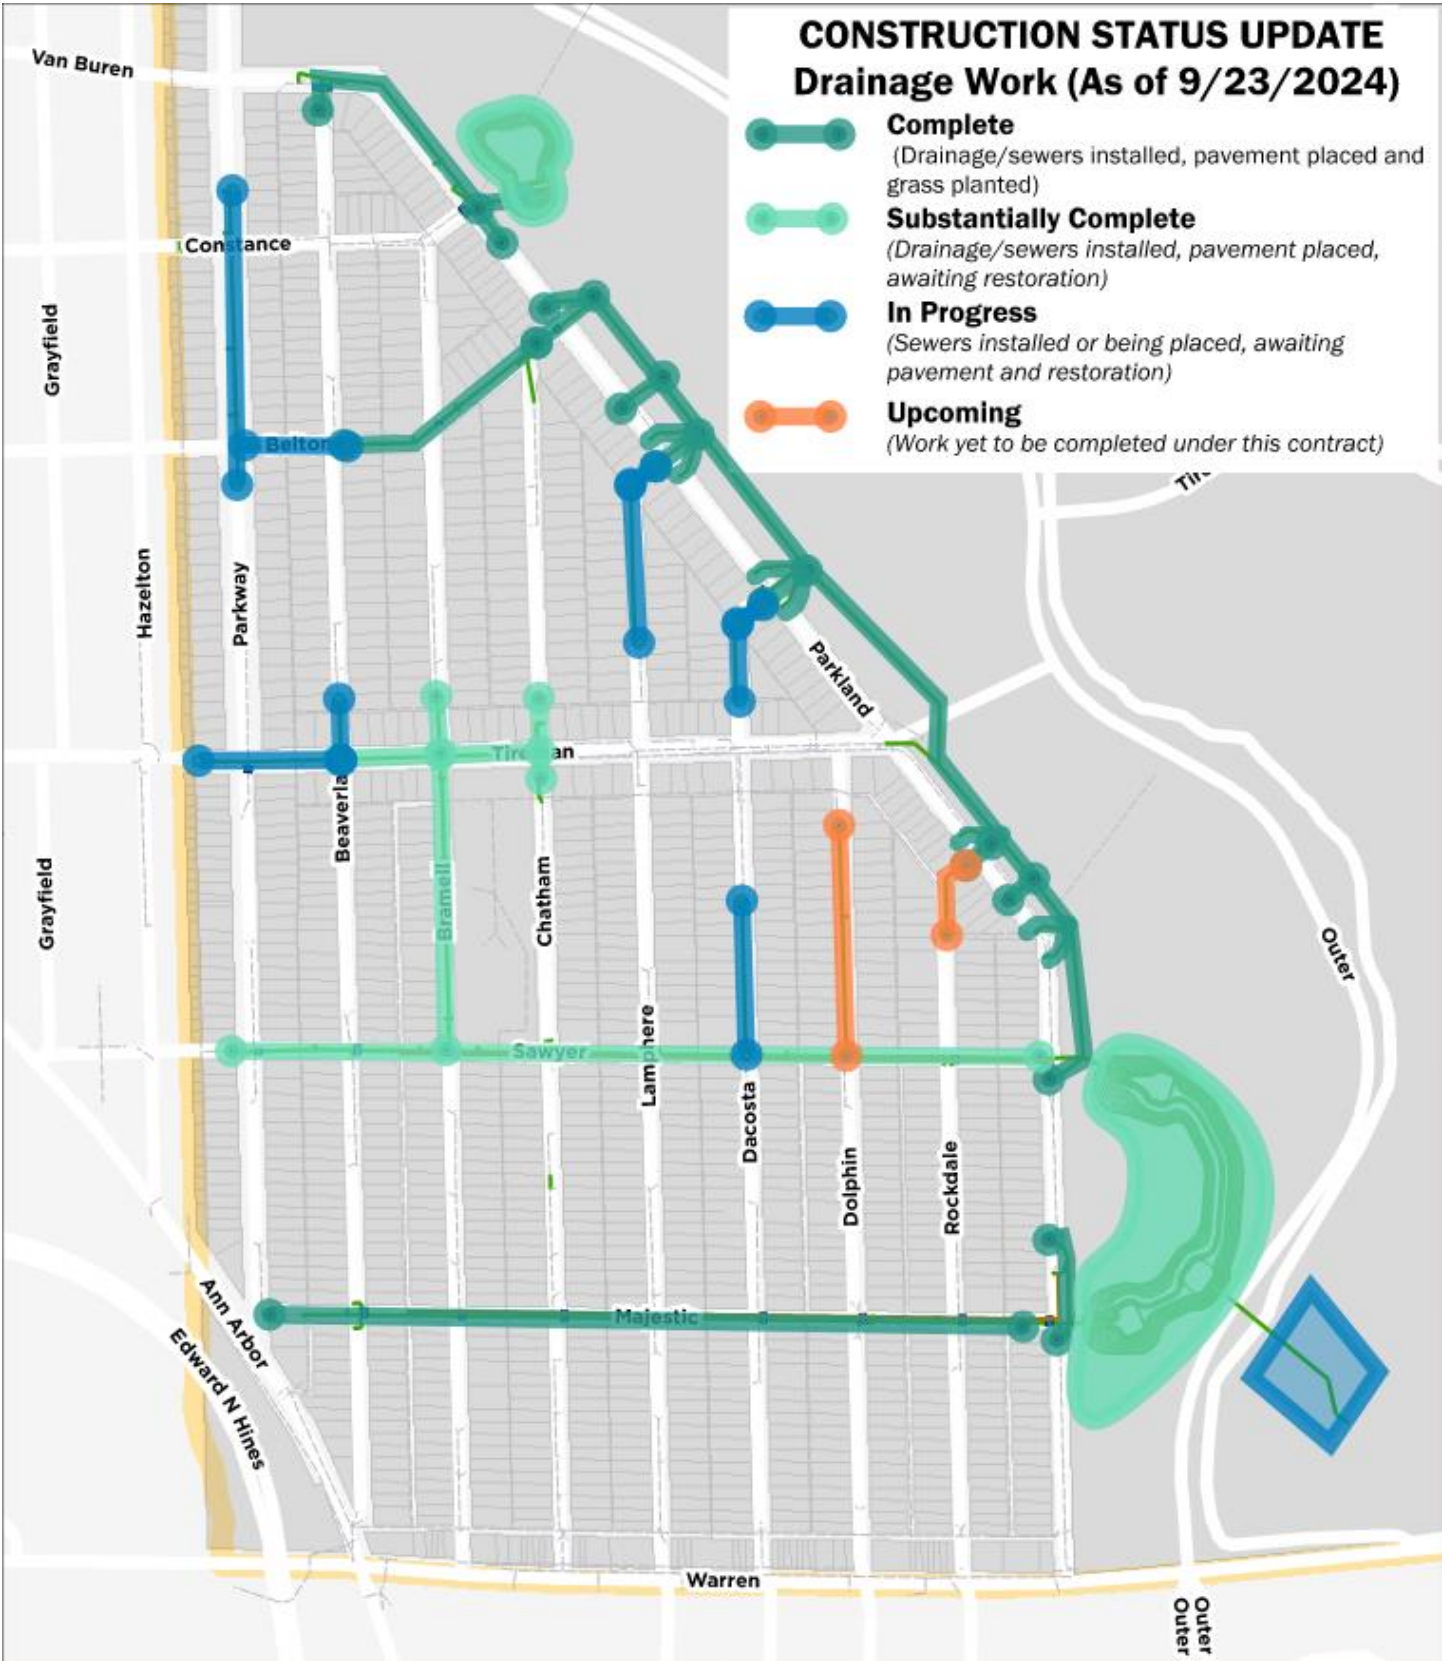

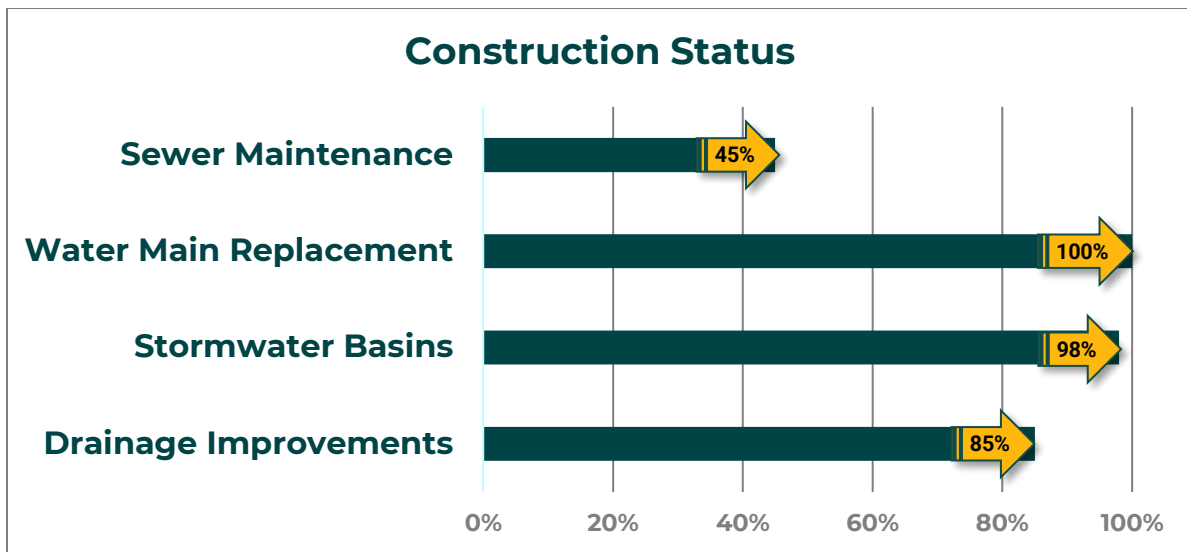

Quarterly Construction Meeting

Join us for updates on the Far West Detroit Stormwater Improvement Project. Members of the project team will be available to answer your questions.

Thursday, October 3, 2024 at 6:00PM
Dixon Educational Learning Academy
8401 Trinity Street, Detroit MI 48228

Thank You!

We know construction projects can be messy, dirty, and noisy. The work can also be inconvenient for our residents as you move to and from your homes. **DWSD understands this and appreciates your patience throughout this process as we work to upgrade the infrastructure in your neighborhood.**

DWSD is available to answer your questions or concerns regarding construction in Far West Detroit. If you have a question, please call us at 313-880-2812 or [email us at dwsd-publicaffairs@detroitmi.gov](mailto:dwsd-publicaffairs@detroitmi.gov).
